

QBS - PROJECT MODULE

STANDARD OPERATING PROCEDURE MANUAL

[Project Settings](#) | [Masters](#) | [Task Management](#) | [Timesheets](#) | [Expenses](#) | [Billing](#) | [Material Tracking](#) | [Reports](#)

Version 1.0 | September 2026
Prepared for QBS Project Module implementations
Internal controlled working document

Document Control

Document Title	QBS Project Module SOP Manual	Version	1.0
Document Owner	Project / PMO Process Owner	Prepared By	Q10 Analytics Pvt. Ltd.
Approved By		Effective Date	
Review Cycle	Annual / major release	Classification	Internal Use
Supersedes	New document	Next Review	

How to Use this Manual

This manual defines recommended operating procedures and control checklists for an QBS Project Module implementation. Exact field names, permissions and screen labels can vary by client configuration. Where a client-specific workflow differs, the approved configuration and role matrix shall prevail. Screenshots can be inserted later as implementation-specific work instructions without changing the underlying SOP controls.

Project Module Control Philosophy

- One authoritative Project master with a unique Project Code per project.
- Task, timesheet and expense entries should be traceable to an approved project plan and assignment.
- Approvals follow the configured project authority matrix; billing and expense postings should not bypass workflow.
- Exceptions use approved correction procedures with an audit trail.
- Monthly project financials are reconciled and closed before revenue recognition and reporting handover.

SOP Index

SOP	Module / Process	Primary Owner
01	Project Settings & Configuration	Project Administrator
02	Customer, Employee & Cost Center Master Setup	Project Administrator
03	Project Creation & Team Assignment	Project Manager
04	Task Management & Scheduling	Project Manager
05	Project Templates & Milestones	Project Manager
06	Timesheet Management	Project Manager
07	Expense Management	Accounts Team
08	Billing & Invoicing	Accounts Team
09	Material & Resource Tracking	Project Manager / Stores
10	Project Approval Matrix	Project Administrator
11	Reports & Monitoring	Project Manager / Management
12	Project Closure & Monthly Review	Project Manager / Accounts
13	Project Exception & Troubleshooting	Project Administrator

SOP 01: Project Settings & Configuration

Document	QBS Project Module SOP Manual	Version	1.0
SOP Code	QBS-PROJECT-01	Process Owner	Project Administrator
Effective Date	To be approved	Review Cycle	Annual / on major system change
Frequency	As required	Classification	Internal Use

Purpose

Ensure the Project module is configured with approved defaults, permissions and numbering before any project is created.

Scope

Project Settings, default project type, numbering series, permission rules, currency/UOM defaults and module-level configuration.

Roles and Responsibilities

Role	Responsibility
Project Administrator	Configures Project Settings, permissions and defaults.
PMO / Process Owner	Approves configuration standards.
System Administrator	Applies role-based access as per approved matrix.

Prerequisites

- Approved project coding convention is defined.
- Company, currency and cost center structure exist.
- Role-based access matrix is approved.

Procedure

1. Configuring **Project Settings** (defaults, permissions).
2. Setting up **Masters**: Customers, Employees, Cost Centers.
3. Creating the **Project** with timelines and manager assignment.
4. Defining **Tasks** with owners, deadlines, and dependencies.
5. Enabling **Timesheets** for effort tracking.
6. Configuring **Expense Categories** and approval workflows.
7. Deciding on **Billing Method** (milestone, hourly, or fixed).
8. Linking **Warehouses/Items** if material tracking is needed.
9. Starting daily operations: task updates, timesheets, expenses, invoicing.
10. Monitoring progress with built-in reports.

Controls and Exceptions

- Do not change global Project Settings without PMO approval; changes affect all live projects.
- Numbering series must not be altered after projects are live without a reconciliation plan.
- Test configuration changes in a non-production project before applying broadly.

Checklist

✓	Check Point	Status / Remarks
☐	Project Settings reviewed and approved.	
☐	Numbering series configured correctly.	
☐	Default holiday list/working hours set.	
☐	Permission rules applied per role matrix.	
☐	Currency/costing defaults verified.	
☐	Configuration tested on sample project.	
☐	Change documented.	

SOP 02: Customer, Employee & Cost Center Master Setup

Document	QBS Project Module SOP Manual	Version	1.0
SOP Code	QBS-PROJECT-02	Process Owner	Project Administrator
Effective Date	To be approved	Review Cycle	Annual / on major system change
Frequency	As required	Classification	Internal Use

Purpose

Ensure Customer, Employee and Cost Center masters are complete and correctly linked before they are used on projects.

Scope

Creation and maintenance of Customer records (CRM), Employee profiles (linked to HR/user IDs), Cost Centers and Item Groups used for material tracking.

Roles and Responsibilities

Role	Responsibility
Admin	Creates/maintains Customer and Cost Center masters.
HR/HRMS Administrator	Ensures Employee profiles are updated and linked to user IDs.
Project Manager	Validates masters required for a specific project before use.

Prerequisites

- Client/customer approved details available (name, billing address, GSTIN where applicable).
- Employee master is current.
- Approved cost center structure exists.

Procedure

1. Search the existing Customer master to avoid duplicate client records.
2. Create/update the Customer record under CRM with approved legal name, billing details and GST information.
3. Confirm Employee profiles exist in the HR module and are linked to the correct system User ID.
4. Create Cost Centers required for expense allocation, following the approved chart.
5. Configure Item Groups where inventory/materials will be tracked against projects.
6. Map the default cost center on the customer/project where the implementation supports it.
7. Validate masters with a maker-checker review before they are used on a live project.

Controls and Exceptions

- Never create a duplicate Customer record to work around a data issue; correct the master.
- Cost Center creation/deactivation should follow the finance approval process.
- Employee-user mapping must be verified before granting project access.

Checklist

✓	Check Point	Status / Remarks
☐	No duplicate customer record created.	
☐	Customer GST/billing details verified.	
☐	Employee-user ID mapping confirmed.	
☐	Cost centers created as per approved chart.	
☐	Item groups configured where required.	
☐	Masters independently reviewed.	

SOP 03: Project Creation & Team Assignment

Document	QBS Project Module SOP Manual	Version	1.0
SOP Code	QBS-PROJECT-03	Process Owner	Project Manager
Effective Date	To be approved	Review Cycle	Annual / on major system change
Frequency	As required	Classification	Internal Use

Purpose

Ensure every project is created with complete, approved information and a clearly assigned manager before task planning begins.

Scope

Project creation, customer linkage, start/end dates, project manager assignment, Save & Submit workflow.

Roles and Responsibilities

Role	Responsibility
Project Manager	Creates the project and assigns the team.
Admin	Confirms permission and workflow configuration.
Accounts Team	Confirms billing/customer linkage where relevant.

Prerequisites

- Customer master exists and is approved.
- Project code convention and manager assignment are agreed.
- Approved project charter/scope is available.

Procedure

1. Search Project records to confirm the project does not already exist.
2. Create the Project: enter project name, customer, start date, expected end date and assigned Project Manager.
3. Link the project to the correct cost center and company.
4. Enter estimated budget/costing figures where required by policy.
5. Add team members to the project with their roles.
6. Save the project as Draft and circulate for review where a maker-checker step applies.
7. Save & Submit the project once details are verified.
8. Communicate the project code and manager assignment to the team.

Controls and Exceptions

- Do not submit a project without an assigned Project Manager and customer linkage.
- Project dates should reflect the approved charter; changes need an approved basis.
- Avoid creating a new project to correct a data-entry error; edit the existing record.

Checklist

✓	Check Point	Status / Remarks
☐	Project not duplicated.	
☐	Customer and cost center linked correctly.	
☐	Manager assigned.	
☐	Start/end dates verified.	
☐	Team members added with roles.	
☐	Project Saved & Submitted.	
☐	Project code communicated to team.	

Projects ERPNext

Search

Ctrl+K

Notification

Home

Dashboard

Project

Task

Timesheet

Setup

Reports

Settings

Projects / Project / New Project

Not Saved

Save

Details

Costing

Progress

More Info

Series *

PROJ-.####

From Template

Project Name *

Priority

Medium

Status

Open

Department

Project Type

Is Active

Yes

% Complete Method

Task Completion

Timeline

SOP 04: Task Management & Scheduling

Document	QBS Project Module SOP Manual	Version	1.0
SOP Code	QBS-PROJECT-04	Process Owner	Project Manager
Effective Date	To be approved	Review Cycle	Annual / on major system change
Frequency	Daily	Classification	Internal Use

Purpose

Ensure tasks are planned, assigned and sequenced correctly so progress and dependencies are visible and reliable.

Scope

Task creation, owner assignment, deadlines, dependencies, Gantt Chart and Kanban Board visualisation.

Roles and Responsibilities

Role	Responsibility
Project Manager	Creates tasks, sets dependencies and monitors the schedule.
Team Members	Update task status and report blockers.
Admin	Maintains task status/type configuration.

Prerequisites

- Project is created and submitted.
- Work breakdown structure is agreed.
- Employee availability/assignment is confirmed.

Procedure

1. Break down the project scope into tasks aligned to the agreed work breakdown structure.
2. Create each Task under the project with a clear title, description and owner.
3. Set start/end dates and estimated hours for each task.
4. Define task dependencies so downstream tasks are sequenced correctly.
5. Review the Gantt Chart to confirm the overall schedule is realistic.
6. Use the Kanban Board for day-to-day status tracking (Open, Working, Pending Review, Completed).
7. Update task status as work progresses; flag blockers to the Project Manager promptly.
8. Review overdue/at-risk tasks in a recurring status review.

Controls and Exceptions

- Tasks should not be marked Completed without the owner's confirmation.
- Circular or conflicting dependencies must be resolved before the schedule is finalised.
- Reassigning a task requires Project Manager approval and updated owner communication.

Checklist

✓	Check Point	Status / Remarks
☐	Tasks created for full scope.	
☐	Owners and dates assigned.	
☐	Dependencies defined and reviewed.	
☐	Gantt/Kanban view validated.	
☐	Overdue tasks reviewed.	
☐	Status updates current.	

The screenshot shows the 'New Task' form in the ERPNext application. The form is titled 'Projects / Task / New Task' and has a 'Not Saved' status. The sidebar on the left contains navigation options: Home, Dashboard, Project, Task, Timesheet, Setup, Reports, and Settings. The main form area has tabs for 'Details', 'Dependencies', and 'More Info'. The 'Details' tab is active, showing fields for Subject, Project, Issue, Type, Color, Status (Open), Priority (Low), Weight, and Parent Task. There are also checkboxes for 'Is Group' and 'Is Template', and a 'Timeline' section. At the bottom, there is a 'Task Description' field with a rich text editor toolbar.

SOP 05: Project Templates & Milestones

Document	QBS Project Module SOP Manual	Version	1.0
SOP Code	QBS-PROJECT-05	Process Owner	Project Manager
Effective Date	To be approved	Review Cycle	Annual / on major system change
Frequency	As required	Classification	Internal Use

Purpose

Standardise recurring project types and ensure major deliverables are tracked as milestones.

Scope

Project Template creation and use, Milestone definition, recurring project setup.

Roles and Responsibilities

Role	Responsibility
Project Manager	Defines milestones and applies templates.
Admin	Maintains approved Project Templates.
PMO	Approves template structure for recurring project types.

Prerequisites

- A recurring project type/pattern has been identified.
- Standard task list and typical durations are documented.

Procedure

1. Identify project types that recur frequently enough to justify a template.
2. Build the Project Template with standard tasks, default durations and dependencies.
3. Review and approve the template with PMO before publishing for general use.
4. When creating a new project of that type, apply the template instead of building tasks from scratch.
5. Define Milestones for major deliverables within the project.
6. Link relevant tasks to the milestone they support.
7. Track milestone due dates alongside the overall project schedule.
8. Update the template based on lessons learned from completed projects.

Controls and Exceptions

- Only approved templates should be published for general use.
- Milestone dates should not be moved without documented client/stakeholder agreement.
- Template changes should be version-controlled.

Checklist

✓	Check Point	Status / Remarks
☐	Template reviewed and approved.	
☐	Template applied consistently for recurring project types.	
☐	Milestones defined for major deliverables.	
☐	Tasks linked to milestones.	
☐	Milestone dates tracked and current.	

Projects ERPNext

[Home](#) / [Projects](#) / [Project Template](#) / **New Project Template** Not Saved

Save

☐ Disabled

Tasks

☐	No.	Task *	Subject	
☐	1			

Add row

SOP 06: Timesheet Management

Document	QBS Project Module SOP Manual	Version	1.0
SOP Code	QBS-PROJECT-06	Process Owner	Project Manager
Effective Date	To be approved	Review Cycle	Annual / on major system change
Frequency	Daily	Classification	Internal Use

Purpose

Ensure employee effort is captured accurately against the correct project and task for costing and billing.

Scope

Timesheet entry, task linkage, review and approval of logged hours.

Roles and Responsibilities

Role	Responsibility
Team Members	Log hours against assigned tasks.
Project Manager	Reviews and approves timesheets.
Accounts Team	Uses approved timesheets for costing/billing.

Prerequisites

- Employee is assigned to the project/task.
- Approved working hours/shift information is available.

Procedure

1. Confirm the employee is mapped to the project and specific task before they log time.
2. Employee records daily/weekly hours against the correct task in the Timesheet.
3. Include a brief description of work performed for audit and billing clarity.
4. Submit the Timesheet for Project Manager review.
5. Project Manager reviews entries for accuracy against task progress.
6. Approve or return the timesheet with comments for correction.
7. Approved timesheets flow to costing/billing per the configured billing method.
8. Investigate missing timesheets against expected effort weekly.

Controls and Exceptions

- Timesheets should not be approved without a reasonable check against task progress.
- Missing Timesheets are usually caused by the employee not being assigned to the project/task; verify assignment first.
- Retrospective timesheet edits after billing should follow a controlled correction process.

Checklist

✓	Check Point	Status / Remarks
☐	Employee-task assignment verified.	
☐	Hours logged against correct task.	
☐	Description of work included.	
☐	Timesheet reviewed by manager.	
☐	Approved/returned with comments.	
☐	Missing timesheets followed up weekly.	

Projects ERPNext

Search

Ctrl+K

Notification

Home

Dashboard

Project

Task

Timesheet

Setup

Reports

Settings

Getting Started

Administrator

admin@example.com

Projects / Timesheet / New Timesheet Not Saved

Start Timer

Save

Details

Billing

Series *

TS-.YYYY.-

Status

Draft

Company

Project

Customer

Currency

INR

Exchange Rate

1.000

Employee Detail

Employee

Time Sheets

☐	No.	Activity Type	From Time	Hrs	Project	Is Billa...	
☐	1			0.000			

SOP 07: Expense Management

Document	QBS Project Module SOP Manual	Version	1.0
SOP Code	QBS-PROJECT-07	Process Owner	Accounts Team
Effective Date	To be approved	Review Cycle	Annual / on major system change
Frequency	As required	Classification	Internal Use

Purpose

Ensure project-related expenses are recorded, tagged and approved correctly for accurate cost tracking.

Scope

Recording of travel, subcontracting and material expenses; project/cost center tagging; approval workflow.

Roles and Responsibilities

Role	Responsibility
Team Members	Submit expense claims tagged to the project.
Project Manager	Reviews and approves project expenses.
Accounts Team	Posts approved expenses and reconciles cost centers.

Prerequisites

- Expense categories and approval limits are configured.
- Project and cost center are correctly linked.

Procedure

1. Employee records the expense (travel, subcontracting, materials, etc.) with supporting evidence.
2. Tag the expense to the correct project and cost center.
3. Select the correct expense category as configured in the system.
4. Submit the expense claim for Project Manager approval.
5. Project Manager reviews the claim against project budget and scope.
6. Approve or reject with comments; rejected claims return to the employee for correction.
7. Accounts Team posts approved expenses and reconciles against the cost center.
8. Investigate any expense not visible on the expected project report.

Controls and Exceptions

- Expenses not visible on a project report are usually a tagging issue; verify project/cost center tagging first.
- Expenses should not be approved beyond the configured authority limit.
- Recurring miscategorised expenses should trigger a review of category configuration.

Checklist

✓	Check Point	Status / Remarks
☐	Expense tagged to correct project/cost center.	
☐	Correct category selected.	
☐	Supporting evidence attached.	
☐	Approved within authority limit.	
☐	Posted and reconciled by Accounts.	
☐	Visibility on project report confirmed.	

SOP 08: Billing & Invoicing

Document	QBS Project Module SOP Manual	Version	1.0
SOP Code	QBS-PROJECT-08	Process Owner	Accounts Team
Effective Date	To be approved	Review Cycle	Annual / on major system change
Frequency	Monthly / milestone-based	Classification	Internal Use

Purpose

Ensure project invoices are generated accurately per the agreed billing method and comply with GST requirements.

Scope

Invoice generation linked to projects, billing method selection (milestone, hourly, fixed fee), GST compliance for Indian clients.

Roles and Responsibilities

Role	Responsibility
Accounts Team	Generates invoices and manages revenue recognition/GST compliance.
Project Manager	Confirms billable progress/hours before invoicing.
Customer	Receives and settles invoices (external).

Prerequisites

- Billing method for the project is agreed and configured.
- Approved timesheets/milestones/expenses are available as billing basis.

Procedure

1. Confirm the project's billing method: milestone-based, hourly, or fixed fee.
2. For milestone billing, confirm the milestone is marked complete and approved before invoicing.
3. For hourly billing, use approved Timesheets as the billing basis.
4. For fixed-fee billing, follow the agreed payment schedule in the contract.
5. Generate the invoice linked to the project and customer.
6. Verify GST details (GSTIN, place of supply, HSN/SAC) for Indian clients before submission.
7. Route the invoice for approval per the finance authority matrix.
8. Share the invoice with the customer and track payment status.
9. Reconcile invoiced amounts against the project's Revenue Report monthly.

Controls and Exceptions

- Do not invoice a milestone that has not been approved as complete.
- Invoice errors are usually due to an incorrect billing method or project linkage; verify both before reissuing.
- GST fields must be verified before invoice submission; do not backdate corrections without an approved basis.

Checklist

✓	Check Point	Status / Remarks
☐	Billing method confirmed.	
☐	Billing basis (milestone/timesheet/schedule) verified.	
☐	GST details verified.	
☐	Invoice linked to correct project/customer.	
☐	Invoice approved per authority matrix.	
☐	Payment status tracked.	
☐	Monthly reconciliation completed.	

Invoicing ERPNext

Q Search

Ctrl+K

Notification

Home

Dashboard

Chart of Accounts

Receivables

Customer

Sales Invoice

Credit Note

Accounts Receivable

Payables

Supplier

Purchase Invoice

Debit Note

Accounts Payable

Payments

Getting Started

Administrator admin@example.com

Invoicing / Sales Invoice / New Sales Invoice Not Saved

Actions

Set Invoice Details

Get Items From

Save

Details

Payments

Address & Contact

Terms

More Info

Series *

SINV-.YY.-

Customer *

Customer PO/WO

Posting Date *

18-09-2026

Posting Time

12:12:18

Payment Due Date *

☐ Include Payment (POS)
 ☐ Is Return (Credit Note)
 ☐ Is Rate Adjustment Entry (Debit Note)
 Issue a debit note with 0 qty against an existing Sales Invoice
☐ Consider for Tax Withholding

☐ Edit Posting Date and Time

Title

Items

Scan Barcode

☐ Update Stock

No.	Items	Quantity	UOM *	Rate (L...	Amoun...	Warehouse	Work O...	
1		0		₹ 0.00	₹ 0.00			

SOP 09: Material & Resource Tracking

Document	QBS Project Module SOP Manual	Version	1.0
SOP Code	QBS-PROJECT-09	Process Owner	Project Manager / Stores
Effective Date	To be approved	Review Cycle	Annual / on major system change
Frequency	As required	Classification	Internal Use

Purpose

Ensure materials issued to projects are tracked accurately and consumption is not misallocated.

Scope

Linking warehouses/items to projects, material issue, consumption tracking, resource utilisation.

Roles and Responsibilities

Role	Responsibility
Project Manager	Requests material issue for the project.
Stores/Inventory Team	Issues materials from stock against the project.
Admin	Configures warehouse/item linkage.

Prerequisites

- Item Groups and warehouses relevant to the project exist.
- Approved bill of materials/consumption plan is available where applicable.

Procedure

1. Link the relevant warehouse(s) and items to the project before material movement begins.
2. Raise a material request against the project for required items.
3. Stores issues materials from stock, tagging the issue to the project.
4. Track consumption against the plan; investigate significant variances.
5. Reconcile stock issued against project requirements periodically.
6. Review resource utilisation (employee workload) alongside material usage for full project cost visibility.
7. Report any misallocated material issue for correction with an approved basis.

Controls and Exceptions

- Material issue must always be tagged to the correct project to prevent misallocation.
- Stock issued without a linked project/cost center should be investigated before period close.
- Reversals/corrections to material issue require an approved basis and audit trail.

Checklist

✓	Check Point	Status / Remarks
☐	Warehouse/items linked to project.	
☐	Material requests raised and approved.	
☐	Issues tagged to correct project.	
☐	Consumption reconciled against plan.	
☐	Resource utilisation reviewed.	
☐	Misallocations corrected with approval.	

Stock ERPNext

Search

Notification

Home

Dashboard

Stock Entry

Purchase Receipt

Delivery Note

Material Request

Pick List

Tools

Setup

Reports

Settings

Getting Started

Administrator
admin@example.com

Stock / Material Request / New Material Request

Not Saved

Get Items From Save

Details Terms More Info

Series *
MAT-MR-.YYYY.-

Transaction Date *
18-09-2026

Site

Required By

Request By

Price List
Standard Buying

Purpose *
Purchase

Items

Scan Barcode

Set Warehouse

No.	Item Code *	Item Name	Required By *	Quantit...	Warehouse	UOM *
☐	1			0.000		

Add row Add multiple

Download Upload

SOP 10: Project Approval Matrix

Document	QBS Project Module SOP Manual	Version	1.0
SOP Code	QBS-PROJECT-10	Process Owner	Project Administrator
Effective Date	To be approved	Review Cycle	Annual / on major system change
Frequency	As required	Classification	Internal Use

Purpose

Ensure project creation, task, expense, timesheet and invoicing approvals follow a defined authority matrix.

Scope

Approval hierarchy for project creation, budget changes, expense claims, timesheets and invoices.

Roles and Responsibilities

Role	Responsibility
PMO/Admin	Maintains and publishes the approval matrix.
Project Manager	First-level approver for tasks, timesheets and expenses.
Finance/Accounts	Approver for invoicing and budget-related exceptions.

Prerequisites

- Organisation approval hierarchy is defined and documented.
- System role/permission configuration matches the approved matrix.

Procedure

1. Document the approval matrix for each transaction type: project creation, budget change, timesheet, expense, invoice.
2. Configure system roles/permissions to reflect the approved matrix.
3. Test each approval workflow with a sample transaction before go-live.
4. Publish the matrix to Project Managers, Team Members and the Accounts Team.
5. Review the matrix periodically for role changes (new joiners, transfers, exits).
6. Update permissions immediately when an approver role changes.
7. Audit a sample of approved transactions periodically against the published matrix.

Controls and Exceptions

- Direct data changes should not bypass the configured approval workflow.
- Approver access must be removed promptly on role change or exit.
- Matrix changes require PMO/Admin sign-off and version control.

Checklist

✓	Check Point	Status / Remarks
☐	Approval matrix documented and current.	
☐	System permissions match matrix.	
☐	Workflow tested end-to-end.	
☐	Matrix published to stakeholders.	
☐	Approver changes updated promptly.	
☐	Periodic audit completed.	

SOP 11: Reports & Monitoring

Document	QBS Project Module SOP Manual	Version	1.0
SOP Code	QBS-PROJECT-11	Process Owner	Project Manager / Management
Effective Date	To be approved	Review Cycle	Annual / on major system change
Frequency	Weekly / Monthly	Classification	Internal Use

Purpose

Provide reliable, timely visibility into project progress, cost and profitability using standard reports.

Scope

Progress Report, Timesheet Report, Expense Report, Revenue Report, Cashflow Report, Resource Utilization Report and Profitability Analysis.

Roles and Responsibilities

Role	Responsibility
Project Manager	Reviews progress and resource reports regularly.
Management	Reviews profitability and cashflow reports.
Accounts Team	Reviews revenue and expense reports.

Prerequisites

- Underlying task, timesheet, expense and billing data is current.
- Reporting cadence (weekly/monthly) is agreed.

Procedure


1. Review the Progress Report to confirm task completion against plan.
2. Review the Timesheet Report to confirm hours logged match expected effort.
3. Review the Expense Report for cost breakdown by category and project.
4. Review the Revenue Report to confirm invoices/payments are current.
5. Review the Cashflow Report for a profitability snapshot.
6. Review the Resource Utilization Report to identify overloaded or underutilised employees.
7. Run Profitability Analysis comparing budget vs. actuals for the project.
8. Share monthly reports with the client/stakeholders for transparency.
9. Flag significant variances for management review and corrective action.

Controls and Exceptions

- Reports should be reconciled against source data before being shared externally.
- Significant budget-to-actual variances require documented explanation.
- Report distribution to clients should follow the approved communication process.

Checklist

✓	Check Point	Status / Remarks
☐	Progress Report reviewed.	
☐	Timesheet/Expense Reports reviewed.	
☐	Revenue/Cashflow Reports reviewed.	
☐	Resource Utilization Report reviewed.	
☐	Profitability Analysis completed.	
☐	Reports shared per agreed cadence.	
☐	Variances flagged and actioned.	

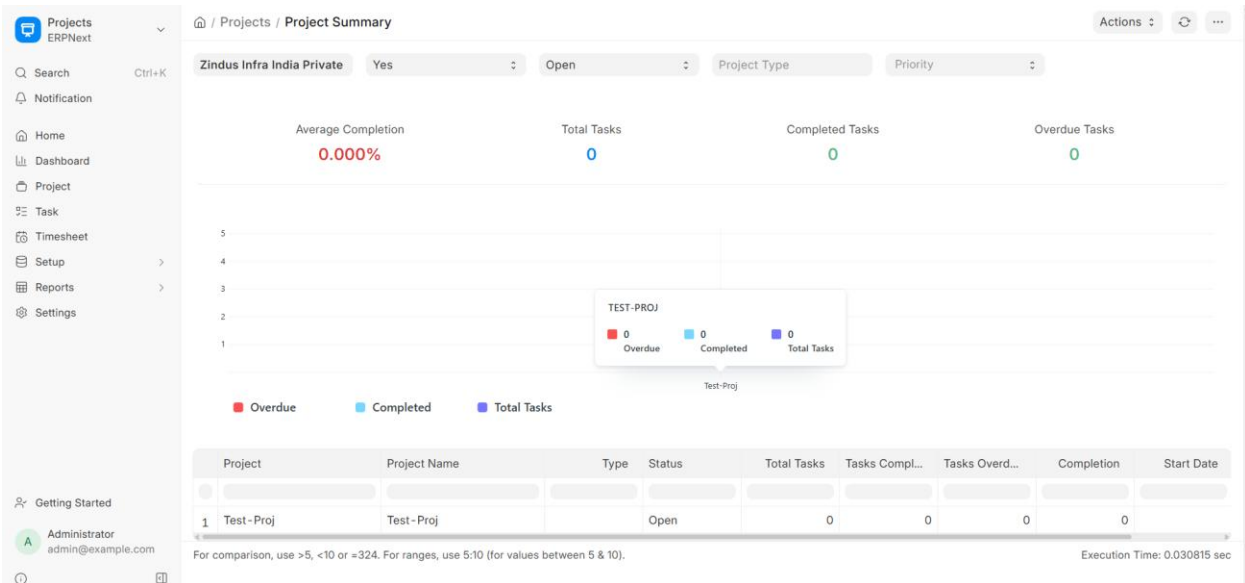

SOP 12: Project Closure & Monthly Review

Document	QBS Project Module SOP Manual	Version	1.0
SOP Code	QBS-PROJECT-12	Process Owner	Project Manager / Accounts
Effective Date	To be approved	Review Cycle	Annual / on major system change
Frequency	Monthly	Classification	Internal Use

Purpose

Ensure projects are formally closed and monthly project financials are reconciled before handover to accounts/payroll.

Scope

Project completion confirmation, outstanding task/expense/invoice clearance, monthly reconciliation and closure.

Roles and Responsibilities

Role	Responsibility
Project Manager	Confirms completion and clears outstanding items.
Accounts Team	Reconciles billing and revenue before closure.
PMO/Admin	Signs off on project closure.

Prerequisites

- All milestones/tasks are marked complete or formally closed.
- Outstanding timesheets, expenses and invoices are identified.

Procedure

1. Confirm all tasks and milestones are completed or formally closed, with reason recorded for any exceptions.
2. Clear pending timesheets and expense approvals before month-end.
3. Reconcile invoiced amounts against the Revenue Report.
4. Confirm final Profitability Analysis (budget vs. actual) is complete.
5. Obtain Project Manager and Accounts sign-off for monthly closure.
6. Update the project status to Completed/Closed once sign-off is obtained.
7. Archive project documentation for audit purposes.
8. Review recurring issues from the period for root-cause/preventive action.

Controls and Exceptions

- Do not close a project with unresolved billing discrepancies.
- Monthly closure should not proceed until pending timesheets/expenses are cleared.
- Reopening a closed project requires PMO approval and an audit trail.

Checklist

✓	Check Point	Status / Remarks
☐	Tasks/milestones confirmed complete.	
☐	Pending timesheets/expenses cleared.	
☐	Invoices reconciled with revenue report.	
☐	Profitability analysis finalised.	
☐	Sign-off obtained.	
☐	Project status updated.	
☐	Documentation archived.	

SOP 13: Project Exception & Troubleshooting

Document	QBS Project Module SOP Manual	Version	1.0
SOP Code	QBS-PROJECT-13	Process Owner	Project Administrator
Effective Date	To be approved	Review Cycle	Annual / on major system change
Frequency	As required	Classification	Internal Use

Purpose

Provide a consistent method for diagnosing and resolving Project Module issues.

Scope

Missing timesheets, expenses not visible on reports, invoice errors and other common exceptions.

Roles and Responsibilities

Role	Responsibility
Project Manager	Reports and triages exceptions.
Admin	Investigates configuration/master data issues.
Accounts Team	Investigates billing/GST exceptions.

Prerequisites

- Issue description, project, employee and date/time are captured.
- Recent configuration changes are known.

Procedure

1. Classify the issue: assignment/master data, configuration, billing, or system/integration.
2. For missing timesheets, verify the employee is assigned to the project/task.
3. For expenses not visible on reports, verify project/cost center tagging.
4. For invoice errors, verify the billing method and project/customer linkage.
5. Trace the data flow layer by layer: task/timesheet/expense entry → project record → report/invoice.
6. Test the fix against the original scenario before closing the issue.
7. Check for duplicate or unintended records created during correction.
8. Record root cause, corrective action and preventive action for recurring issues.

Controls and Exceptions

- Do not proceed to direct data correction before the root cause is understood.
- Preserve evidence (screenshots, logs) before reprocessing.
- Bulk corrections require backup, sample validation and post-change reconciliation.

Checklist

✓	Check Point	Status / Remarks
☐	Issue and project/employee captured.	
☐	Root cause classified.	
☐	Assignment/tagging/billing verified as applicable.	
☐	Fix tested on original scenario.	
☐	Duplicate check completed.	
☐	Root cause and preventive action documented.	

Project Module Flow Diagram

The diagram below illustrates the end-to-end QBS Project Module flow from setup through reporting.



Master QBS Project Module Go-Live / Periodic Control Checklist

Area	Control Check	Status	Remarks / Owner
Masters	Project codes unique and complete	☐	
Masters	Customer, Employee and Cost Center masters validated	☐	
Masters	Item Groups and warehouses linked where required	☐	
Project Setup	Project Settings and numbering series validated	☐	
Project Setup	Permission rules applied per role matrix	☐	
Task & Schedule	Tasks, dependencies and Gantt/Kanban tested	☐	
Task & Schedule	Project Templates and Milestones validated	☐	
Timesheet & Expense	Timesheet submission and approval tested	☐	
Timesheet & Expense	Expense tagging to project/cost center tested	☐	
Billing	Billing method configured and tested for each project type	☐	
Billing	GST fields verified for Indian clients	☐	
Material & Resources	Material issue and consumption tracking tested	☐	
Material & Resources	Resource Utilization Report reviewed	☐	
Security	Roles and permissions reviewed for least privilege	☐	
Security	Separated/inactive users disabled	☐	
Operations	Daily exception-monitoring responsibility assigned	☐	
Operations	Monthly closure and reconciliation calendar issued	☐	
Support	Issue escalation matrix and support contacts published	☐	
Support	Backup/change/reprocessing procedure documented	☐	
Governance	SOP training completed for PM, team and accounts	☐	

Monthly Project Control Sign-off

Control	Owner	Status	Remarks
Timesheet approvals reconciled	Project Manager	☐	
Pending expense approvals cleared	Project Manager / Accounts	☐	
Invoices reconciled with revenue report	Accounts Team	☐	
Project closure sign-offs completed	Project Manager / PMO	☐	
Material issue reconciliation completed	Stores / PM	☐	
Inactive users / stale approvers reviewed	Admin	☐	
Recurring incidents reviewed for RCA/CAPA	PMO / Admin	☐	

Revision History

Version	Date	Change	Prepared By	Approved By
1.0	September 2026	Initial QBS Project Module SOP Manual	Q10 Analytics Pvt. Ltd.	
